STIVEN CATALYST

SECOND SERIES · NOVEMBER 2026

MANAGEMENT REVIEW

Management without theatre.



OPERATIONS

KANBAN: THE LIMIT ON WORK IN PROCESS

Toyota's supermarket method of 1954, a BBC Worldwide team that capped its boards, pull as a limit on open work, judges in Rome who kept fewer cases going, four flow measures and a card for one board.

37% shorter average lead time in 12 months for a nine-person software team at BBC Worldwide that worked with kanban boards and limits on work in process.

MIDDLETON & JOYCE, 2012

INSIDE

COVER STORY

The next process is the customer

PAGE 03

WHAT THE RESEARCH SAYS

Fewer cases at once

PAGE 06

TOOL OF THE ISSUE

One board, with limits

PAGE 08

NO. 66 · OPERATIONS

In this issue

A board full of cards looks like a busy team. Often it belongs to a team that has started more than it can finish. Kanban answers with a limit on work in process: how many things may be open at once, and what happens when that number is reached.

In 1954 Toyota had each process collect its parts from the one before, instead of having them pushed on. Half a century later, a team at BBC Worldwide put limits on its boards and delivered sooner and more evenly. Two researchers of operations argue that pull is, in essence, a cap on work in process. In Rome, six judges who kept fewer cases open at once finished them sooner. The Kanban Guide names four measures; a card helps set up one board.

Stiven Janaqi EDITOR · STIVEN CATALYST

03 COVER STORY
The next process is the customer

04 THE NUMBERS
Limits on the board

05 THE MODEL
Pull is a limit

06 WHAT THE RESEARCH SAYS
Fewer cases at once

07 HOW IT IS MEASURED
Four measures, and the oldest card

08 TOOL OF THE ISSUE
One board, with limits

09 SOURCES
Sources and method

HOW TO READ THIS ISSUE

Figure
Every figure has its source and year at the foot of its page.

Our reading
Where the editors interpret rather than the research, it says so.

Practice
The steps and the card are proposals to try, not research results.

COVER STORY

The next process is the customer

According to Toyota's own history, every part in its machining plant once travelled with a voucher and was carried on to the next plant whether that plant needed it or not. Parts piled up, and assembly built whatever it had parts for.

Early in the month, assembly reached roughly half the plan. At the end of the month, once all the parts were in, the conveyors ran faster to catch up, staffed by the same people who had stood waiting for parts at the start. In 1954, as volumes grew, Toyota introduced what it called the supermarket method.

“The subsequent process is the 'customer' and the prior process is the 'supermarket'.”

01
Supermarket
the earlier process: it holds parts and replaces only what was taken

02
Customer
the later process: it takes what it needs, when it needs it

03
Kanban
the card added later: product name, number and quantity

OUR READING

Push moves work on once it is finished. Pull starts work once there is room for it.

Source: Toyota Motor Corporation, 2012


Toyota's history traces the idea to a 1954 trade-press report on a Lockheed aircraft plant, at a time when supermarkets were still rare in Japan. Other accounts credit Taiichi Ohno's look at US supermarkets; we could not check his book, so we follow Toyota.

THE NUMBERS

Limits on the board

In April 2008 a nine-person software team at BBC Worldwide drew its stages on kanban boards and put each piece of work on a card. More work was in process than anyone had realised. Peter Middleton and David Joyce studied a year of the team's data.

WORKING DAYS, ONE BBC WORLDWIDE TEAM, 2008–2009

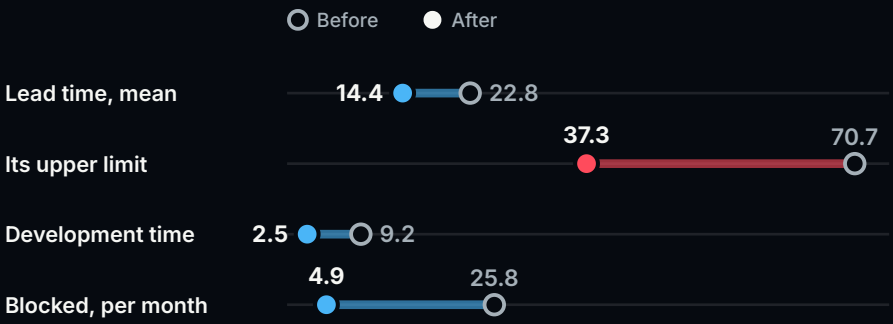

The limits followed the constraints. With fewer testers and analysts than developers, the team set them by what those roles could handle and moved them when the constraints moved. Defects still open and reported each week fell by 24%.

OUR READING

The limit did not make anyone work faster. It made the queue visible, at the stage where it formed.

Source: Peter Middleton & David Joyce, IEEE Transactions on Engineering Management 59(1), 2012

Upper limit: the upper control limit of lead time, a measure of spread (−47%). Development time covers nine months. A single case: the team also broke its work into smaller pieces and grew in skill.

THE MODEL

Pull is a limit

Wallace Hopp and Mark Spearman argued in 2004 that the practitioner literature had simplified “pull” to the point of misunderstanding. Their definition is short: pull is essentially a mechanism for limiting work in process. A kanban card is one such mechanism: no free card, no new start.

A WORKFLOW WITH A LIMIT, AFTER THE KANBAN GUIDE

01	02	03	04
Work item	**Started**	**States, with a limit**	**Finished**
what one card stands for	the point where it counts as open	new work only below the limit	the point where it leaves

David Anderson dates kanban in knowledge work to 2004, when he designed a pull system for a maintenance team at Microsoft. It had no physical board. In his account, the cards went up on a whiteboard at Corbis in 2007, at a team member's suggestion. His book Kanban followed in 2010.

OUR READING

A board without limits only pictures the overload. Add a limit, and it becomes a pull system.

Sources: Wallace J. Hopp & Mark L. Spearman, Manufacturing & Service Operations Management 6(2), 2004 (via Abstract at Crossref); John Coleman & Daniel Vacanti, 2025; David J. Anderson, 2014

The definition is Hopp & Spearman's; the chain follows the elements of a workflow in the Kanban Guide (2025). The history is Anderson's own account. The editors drew the conclusions.

WHAT THE RESEARCH SAYS

Fewer cases at once

Decio Coviello, Andrea Ichino and Nicola Persico studied Italian judges who received the same workload by lottery. Those who juggled more trials at once, instead of working through a few in sequence, took longer to complete their cases. The quality of rulings, measured by appeals, did not suffer.

Then came a test at Rome's labour appeals court. From January 2011, six judges in one section scheduled up front every hearing a new case would need, so that cases finished before new ones crowded in. 44 judges in four other sections carried on as before. The data run from 2005 to 2014.

12%
shorter average case duration, against the other judges

111 days
less per case, by the authors' estimate

OUR READING

The judges started less at once and finished what they had started; the effort stayed the same.

Sources: Decio Coviello, Andrea Ichino & Nicola Persico, Journal of the European Economic Association 13(5), 2015; Robert L. Bray, Decio Coviello, Andrea Ichino & Nicola Persico, Manufacturing & Service Operations Management 18(4), 2016

Not a random assignment: the section's president asked to take part. A difference-in-differences study with six treated judges, supported by a placebo test. Their rulings were also appealed less often. Not every study finds lower WIP better on every measure (see No. 58).

HOW IT IS MEASURED

Four measures, and the oldest card

The Kanban Guide by John Coleman and Daniel Vacanti asks every kanban system to track four flow measures, each counted between the points where the team says work starts and finishes.

01	**Work in process**	items started but not finished
02	**Throughput**	items finished per unit of time
03	**Work item age**	time since an open item started
04	**Cycle time**	time from start to finish

The guide pairs them with a service level expectation, such as “85% of work items will be finished in eight days or less”. At BBC Worldwide the daily stand-up took about 15 minutes at the board: first the cards, then blocked work, then clusters, then priorities.

HYPOTHETICAL EXAMPLE, A RETURNS DESK BOARD ON A MONDAY

Open	14 cards against a limit of 12
Oldest	11 days; 85% usually close within 6

The average looks fine; the oldest card and the overrun show where to act. The board is invented, figures included.

Sources: John Coleman & Daniel Vacanti, 2025; Peter Middleton & David Joyce, IEEE Transactions on Engineering Management 59(1), 2012

The four definitions and the sample expectation come from the Kanban Guide, the stand-up from Middleton & Joyce. How the three averages relate is the subject of No. 58. The example is the editors'.

More in the essay — Ten minutes before the shift: what the team needs to know before the work starts

TOOL OF THE ISSUE

One board, with limits

One team, one flow of work. Before you set any limit, count what is open today; start the limits near that count, and lower them only after a review.

01 Work item and flow what one card stands for; where work starts and finishes

02 Columns and limits each stage, today's count, its limit

03 Pull rule who starts new work, and only below the limit

04 Exceptions what may jump the queue, and who decides

05 Blocked items marked on the card; who removes the block, by when

06 Weekly review oldest card, finished items, is each limit still right

Sources: John Coleman & Daniel Vacanti, 2025; Wallace J. Hopp & Mark L. Spearman, Manufacturing & Service Operations Management 6(2), 2004 (via Abstract at Crossref); Peter Middleton & David Joyce, IEEE Transactions on Engineering Management 59(1), 2012

Suggested by the editors, drawing on the Kanban Guide, Hopp & Spearman and the BBC Worldwide team, which set its limits from its constraints and changed them as the constraints moved.

Open the tool: Shift Handover stivencatalyst.com/tools/shift-handover/

SOURCES AND METHOD

Every figure has a source.

The figures in this issue come from the sources below. The year shows how recent each one is.

75 Years of Toyota: Supermarket Method
Toyota Motor Corporation, 2012
https://www.toyota-global.com/company/history_of_toyota/75years/text/taking_on_the_automotive_business/chapter2/section7/item4.html

Lean Software Management: BBC Worldwide Case Study
Peter Middleton & David Joyce, IEEE Transactions on Engineering Management 59(1), 2012
https://doi.org/10.1109/TEM.2010.2081675

To Pull or Not to Pull: What Is the Question?
Wallace J. Hopp & Mark L. Spearman, Manufacturing & Service Operations Management 6(2), 2004 · via Abstract at Crossref
https://doi.org/10.1287/msom.1030.0028

A Brief History of Kanban for Knowledge Work
David J. Anderson, 2014
https://djaa.com/brief-history-kanban-knowledge-work/

The Inefficiency of Worker Time Use
Decio Coviello, Andrea Ichino & Nicola Persico, Journal of the European Economic Association 13(5), 2015
https://doi.org/10.1111/jeea.12129

Multitasking, Multiarmed Bandits, and the Italian Judiciary
Robert L. Bray, Decio Coviello, Andrea Ichino & Nicola Persico, Manufacturing & Service Operations Management 18(4), 2016
https://doi.org/10.1287/msom.2016.0586

The Kanban Guide
John Coleman & Daniel Vacanti, 2025
https://kanbanguides.org/english/

CORRECTION · 16 OCTOBER 2026

The 24% fall in Middleton and Joyce's study is in defects still open and reported each week; the text first said defects reported by customers, which the study does not say.

EDITORIAL METHOD

Each figure was checked for its year, its publisher and what exactly it measures. Where the publisher's page could not be opened, the figure was checked against independent summaries and is marked “via”. The editors' interpretation is marked “Our reading”. Figures that could not be confirmed are not in the issue.



MANAGEMENT REVIEW

Management without theatre.

Every issue, one management question, checked against the best research.

ALL ISSUES

stivencatalyst.com/magazine/management-review.html

Management Review · No. 66 · November 2026 · Stiven Catalyst
